

INCEPTION REPORT

PRO SME FUND

Functional and Technical Requirements Specification/ Project Requirements Baseline
REFERENCE DOCUMENT

Ver: Pro SME FUND_version 1.1

Disclaimer

This document has been prepared with specific reference to Tender No 7000016311 and serves as a Planning and Implementation Reference Document for the Technical Team, Project Owner, appointed Contractor and any authorized development or support partners involved in the implementation of the Tender.


The content of this document has been developed for alignment, coordination and implementation purposes, with the objective of ensuring that the activities and deliverables undertaken under the Tender remain consistent with the requirements, expectations and objectives established by the Project Owner.

The document and its contents, including its structure, specifications, requirements, concepts, methodologies and related materials, shall be regarded as Project Intellectual Property. The authorized use, access, interpretation, modification and application of the document are vested in the Pro SME FUND – Pro SME Fund Project, subject to the applicable contractual arrangements and authorizations.

Any clarification, interpretation or amendment relating to the content, structure or intended purpose of this document shall be subject to the direction and approval of the Project Owner and/or duly authorized representatives.

No part of this document may be copied, reproduced, distributed, transmitted, published, disclosed, adapted or referenced, whether in whole or in part, without the prior authorization of the Project Owner or other duly authorized party. This restriction applies to both physical and electronic forms of the document.

This Reference Document consolidates the principal expectations and requirements of the Project Owner, including, where applicable:

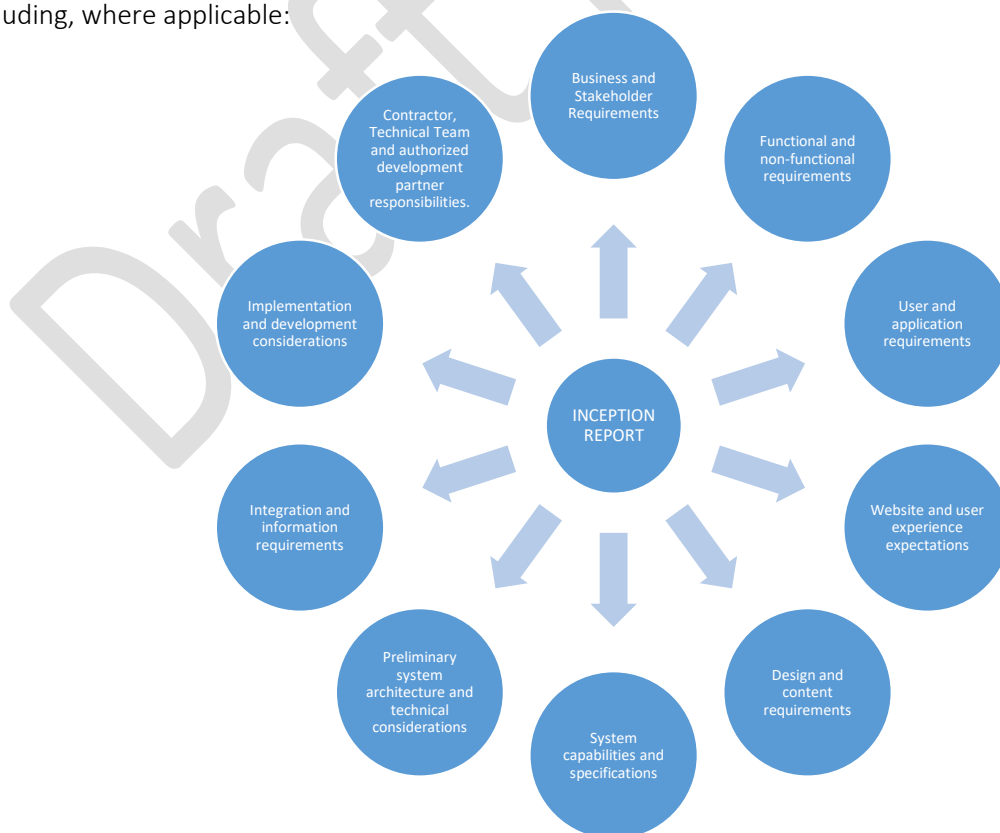

Accordingly, this document is intended to provide a single coordinated reference point for the major project deliverables, supporting consistency between the Project Owner's requirements, the technical implementation and the outputs delivered under the Tender.

Document Amendments and Version Control

This document may be amended, updated or supplemented only by duly authorized persons and in accordance with the applicable approval and change management processes.

Any approved amendment or material update shall result in the document version being updated in chronological numerical order [i.e Ver: Pro SME _ 1.1 > 1.-n]. Each revised version shall clearly indicate the applicable version number, date and nature of the amendment, this is a measure to ensure that all stakeholders can identify and work from the current approved version of the Reference Document.

The latest approved version shall supersede all previous versions unless otherwise expressly stated.

Document Control Principle:

No stakeholder shall rely on an outdated version of this document where a subsequent approved version has been issued.

Overview

The Client (Pro SME FUND) was established through cooperation between the Government of the Republic of Namibia and the Government of the Federal Republic of Germany, within the broader framework of initiatives aimed at strengthening investment promotion, enterprise development and access to development support in Namibia.

The Pro SME FUND serves as an investment and development facilitation platform, connecting Namibian businesses and investment opportunities with relevant investors, development partners and other strategic stakeholders. Through this role, the Pro SME FUND seeks to facilitate, coordinate and strengthen interaction between entrepreneurs, investors and development partners, thereby supporting the development and implementation of viable projects and enterprises.

The Pro SME FUND facilitates investment and development support to Micro, Small and Medium Enterprises (M/SMEs) in Namibia through, among other functions, the promotion of investment opportunities, receipt and processing of applications, preliminary screening, evaluation and assessment of applications, and facilitation of qualifying opportunities towards appropriate support mechanisms and potential investment partners.

To effectively engage its stakeholders and improve accessibility to its services, the Pro SME FUND utilizes a range of communication and engagement platforms, including its interactive digital presence. The website therefore serves as an important interface between the Pro SME FUND, entrepreneurs, investors, development partners and the broader public.

This Reference Document serves as the formal baseline and guiding reference for the implementation of a secure, user-friendly and fit-for-purpose Pro SME FUND website. It consolidates the agreed business, functional, user experience and implementation requirements established by the Project Owner and provides the basis against which the Contractor's implementation activities, deliverables and outputs shall be guided and assessed.

The implementation intervention under Tender Reference No. 7000016311 shall be undertaken in accordance with this Reference Document, together with the applicable Tender requirements, agreed scope, approved specifications and subsequent authorized changes.

Client Endorsement and Acceptance

By signing below, the Client formally endorses and adopts this version of the Reference Document as the approved baseline for implementation.

The undersigned acknowledges that the structure, content, requirements and specifications contained herein represent the Client's agreed business and functional position at the time of approval and shall serve as the reference point for the subsequent design, development, validation and implementation activities.

Any material amendments to the approved baseline shall be subject to the agreed change management and approval process.

Document Authorization

For and on behalf of Pro SME FUND

Name: _____

Designation: _____

Signature: _____

Date: _____

Official Stamp: _____

Key Abbreviations and Interpretation

GIZ	Deutsche Gesellschaft für Internationale Zusammenarbeit (GIZ) GmbH.
Pro SME Fund	The designated fund supporting eligible applicants and enterprises under the Project.
Tender	Formal procurement process for appointing a service provider.
Client	PRO SME FUND, as the project owner and commissioning organization.
CMS	Content Management System.
Contractor	The appointed service provider responsible for project delivery.
Project Technical Team	Team responsible for technical coordination and project implementation.
Website	The digital platform developed under the Project.
Information	Content made available through the website or system.
Data	Digital information captured, processed or stored by the system.
Stakeholders	Parties with an interest in or involvement in the Project.
Users	Persons authorized or intended to use the system or website.

TABLE OF CONTENTS

1. Introduction	8
2. Objectives and Scope of Works	9
3. Approach Methodology	12
4. Work Break Down Structure – Schedule and Milestones	14
5. Roles and Responsibilities	17
6. Resources and Budget	18
7. Risk Management	19
8. Quality Management	21
9. Communication PLAN	23
9.1. Channels of Communication	
9.2. Reporting	
10. Change Management	26

Annexures

Annexure A:	Requirements Gathering
Annexure B:	Preliminary Technical Designs
Annexure C:	Project FORMS
Annexure D:	Project Technical Team Contact Information

1. INTRODUCTION

- 1.1. The document serves as a central reference point from which approved requirements, deliverables, specifications, decisions and other relevant project information may be extracted for implementation, monitoring, reporting and presentation purposes, subject to the applicable document control and information-use provisions.
- 1.2. The primary purpose of this document is to provide a structured basis for translating the Project Owner's business objectives and requirements into clearly defined technical, functional and user experience requirements.
- 1.3. The Terms of Reference (ToR) for the project have been established by the Project Owner and provide the overarching mandate and scope for the assignment. This Reference Document further ensures that the Project Technical is aligned with the implementation requirements and technicalities that are herein translated to translated into practical and measurable outputs.
- 1.4. Where applicable, requirements, recommendations and technical considerations arising from the Technical Team may be consolidated into this document to provide one coordinated reference for the Project Owner, Technical Team, Contractor and authorized project stakeholders, subject to recommended document use and control.
- 1.5. Finally, the Parties ACCEPT this document as the official working baseline throughout the project's implementation.

2. OBJECTIVES AND SCOPE OF WORKS

2.1. This section of the document establishes a common understanding between the Pro SME FUND (Client/Project Owner) and the Contractor/Service Provider regarding the intended outcomes, principal deliverables and implementation expectations of the assignment.

2.2. For ease of reference, and without replacing the detailed requirements contained in the Tender and associated documentation, the following are identified as the principal deliverables of the assignment:

No	Deliverable
1	Project Inception Report
2	Three (3) Website Design Concepts
3	Approved Final Design Prototype
4	Fully Developed and Operational Website
5	AI Chatbot – Trained and Developed
6	Online Application System with Integrated Work Flow Engine
7	Analytics Dashboard – Configured and Operational
8	User Acceptance Testing Report
9	Staff Training Sessions
10	Training Manuals and Technical Documentation
11	Full Intellectual Property and Source Code Transfer
13	Thirty (30) – Day – Post – Launch Support

Reference Websites / Existing Digital Platforms and Design Options

2.3. Relevant website links and digital platforms identified or provided by the Project Owner, Contractor and other relevant stakeholders shall be incorporated into this document as reference material.

2.4. Without deviating from the Project Owner's (TOR) for the Project; The Contractor recommends that the reference process should not be restricted to a fixed number of websites or platforms. A broader range of relevant digital products may be reviewed to identify useful approaches to functionality, user experience, navigation, visual design, content presentation and overall digital interaction.

2.5. It is recommended that the design process first produce a preliminary website prototype to provide the Client with a tangible representation of the proposed direction. At the initial stage, it can be difficult to fully determine the Client's expectations without a visual or functional concept to review. Once the first prototype is available, the Client can provide more specific feedback, recommendations and amendments. Where appropriate and at the Client's discretion - recommendation primarily; up to three alternative design options or significant amendments may then be developed for consideration, based on the Client's feedback.

2.6. This approach encourages active Client involvement from an early stage while allowing requirements and expectations to be progressively refined through practical review of the prototype. The preferred concept can subsequently be redesigned, refined and developed into the final website, incorporating the agreed feedback and improvements.

2.7. The objective is not to replicate existing websites, but to use relevant references and iterative design development to achieve a modern, intuitive and user-centered digital product that is aligned with the Client's expectations and project requirements.

Overall Solution Objective

2.8. In summary, the Contractor shall deliver a comprehensive, secure, scalable and user-friendly digital solution comprising a public-facing interactive website with integrated online application, workflow management and related digital functionalities to support the objectives of the SME Fund Programme.


2.9. The desired solution shall provide an accessible digital interface through which Applicants, stakeholders and the broader public can access relevant information, understand available opportunities and services, submit applications where applicable, and engage with the Pro SME FUND through appropriate digital channels.

2.10. The digital platform shall also provide secured authorized PRO SME FUND personnel with the necessary administrative and operational capabilities to manage website content (CMS),

applications, workflows, communications and relevant information in accordance with the Clients - Organizational guidelines applicable.


High Level Technical, Functional and Integration Requirements

2.11. The website and associated systems shall be responsive across appropriate devices and screen sizes and shall be designed to support interoperability with the Pro SME FUND's existing operational environment, IT infrastructure, systems and applicable third-party services, where such integration is required and technically feasible.



Content Management System

2.12. Customize - Configure and Integrate a fully functional Content Management System (CMS) that enables authorized, non-technical Pro SME FUND personnel to manage (create, edit, publish) and maintain website content without requiring direct developer intervention for routine content administration (user friendly).

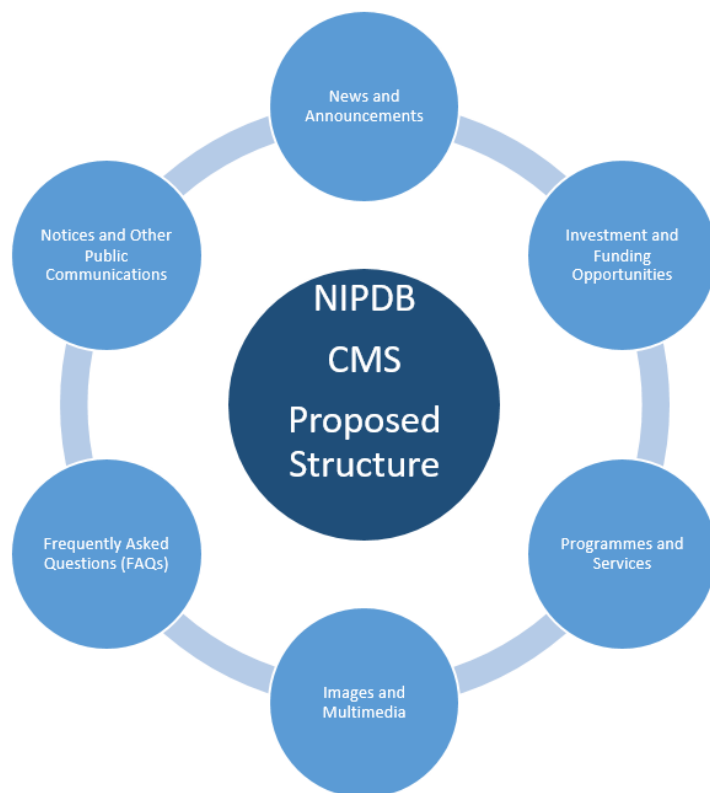

3. APPROACH METHODOLOGY

3.1. This Project follows a structured, end-to-end delivery methodology designed to move systematically from inception and requirements validation through design, development, testing, approval and final handover.

3.2. The methodology is intended to ensure that the solution developed is aligned with the Project Owner's expectations, validated through stakeholder engagement, and progressively refined throughout implementation.

Methodological Flow



Stakeholder Consultation & Inception

3.3. Stakeholder consultation will be undertaken to clarify requirements, understand user needs and confirm operational expectations. The Inception Report will serve as a working document, and its contents may be refined during project execution as additional information, stakeholder inputs and requirements are confirmed.

3.4. Where assumptions are required during inception, these will be clearly identified and presented for review and acceptance. Any confirmed variations will be reflected in the relevant designs, reports and specifications.

Collaborative Delivery & Review

3.5. The Contractor promotes an interactive working arrangement between the Project Owner, Client and project team to address challenges, clarify requirements and make timely corrections.

Regular meetings, milestone reviews and sign-offs will provide structured opportunities to assess progress and confirm deliverables before proceeding to subsequent stages.

Documentation & Quality Control

3.6. The project process will be documented from inception to completion, including clarifications, confirmations, requirements verification, approvals, revisions and milestone deliverables. This provides a clear record of decisions and supports quality control throughout implementation.

Delivery, Implementation & Handover

3.7. The methodology suggested – recommended herein will ensure that project activities are activated and coordinated against the agreed schedule, with deliverables completed to the required standard and within the approved scope. The final stage will include testing (UAT), acceptance, implementation and handover of a fully functional solution, together with the necessary documentation, knowledge transfer and transition arrangements.

3.8. This approach provides a clear delivery logic in which each stage informs and validates the next, reducing uncertainty, encouraging Client participation and ensuring that the final solution reflects the validated requirements and expectations of the Project Owner.

4. WORK BREAK – DOWN STRUCTURE

Task Name	Duration	Start	Finish	Resource Names
WBS _ PROJECT SCHEDULE FOR TENDER NO: 7000016311				
<u>Reference Terms</u>				
1 Week = 5 days, Monday to Friday / 7 days on schedule = 1 week excl. weekends				
Scheduled Activities may be fast tracked				
Major Milestones [M] assigned to Resource may be delegated to Project Team				
Support Activities under Major Milestones subject to same period for execution - competition				
Requirements Planning - INCEPTION REPORT [M1]	7 days	Wed 8/19/26	Thu 8/27/26	Contractor
Stakeholder Identification and Consultation - Needs Analysis and Information Gathering				
Validation of Requirements against Technical and Functional Specifications				
Preliminary Design and Development (Prototyping) [M2]	7 days	Wed 8/19/26	Thu 8/27/26	Contractor
Website Designs - Allow review and inputs from Client				
Website Structure and Sitemap				
Content Structure				
User Journeys				
Functional Specifications				
Technical Architecture				
Integration Requirements				
Approve Final Design [M3]	7 days	Fri 8/28/26	Mon 9/7/26	Contractor
Performance Tuning - Debugging and Testing				
Wire Frames and Page Layouts				
User Experience Design				
Visual Design Aligned to Corporate Identify				
Responsive/ Mobile - First Design				
Client Review and Approval				
Fully Developed and Operational Website [M4]	7 days	Tue 9/8/26	Wed 9/16/26	Contractor
Production Environment Setup				
Data/ Content Management				
Final Configuration				
Database and Functionality Development				
Third Party/ API Integration				
Backup and Rollback Procedures				
Go-Live				
Post Launch Monitoring				

AI Chabot Trained and Deployed [M5]	7 days	Tue 9/8/26	Wed 9/16/26	Contractor
Activate - Integrate and Configure plugins				
Demonstrate functionality to Client/ Stakeholder/ Primary Users to confirm UX expectations				
Online Application System with Work Engine Workflow [M6]	7 days	Tue 9/8/26	Wed 9/16/26	Contractor
Activation of CMS				
CMS Configuration				
Content Population				
Demonstrate functionality to Client				
Front - end and Back - end Development				
Content Population				
Analytics and Dashboard Configured [M7]	7 days	Thu 9/17/26	Fri 9/25/26	Contractor
Configure - Enable - Activate - Demonstrate Functional Automation				
Sign-off - Acceptance - Formal/ Acknowledgement				
User Acceptance Testing (UAT) Report [M8]	28 days	Mon 9/28/26	Wed 11/4/26	Contractor
Prepare and Obtain Client Approval on Testing Methodology				
Conduct UAT - Document Outcomes				
Functional Testing				
Security Testing				
Performance Optimization				
Accessibility Checks				
Responsive/ Device Testing				
Browser Compatibility				
Staff Training [M9]	7 days	Mon 9/28/26	Tue 10/6/26	Contractor & PRO SME FUND IT Staff
High Level on System Overview and Navigation of Website and Features for General Users				
High Level on System Functions - Configurations for Operational Users				
Note and Archive Comments and Recommendations from Client				
Training Manuals and Technical Documentation [M10]	7 days	Mon 9/28/26	Tue 10/6/26	Contractor
Finalize and Submit Training Manuals and Technical Document to Client				
CMS/ User Training				
Administrator Training				
Technical Documentation				
Operational Procedures				
Soft Skills Training to Client Operational Users/ Project Technical Team on Structure of Training Manuals/ Materials				
Full Intellectual Property and Source Code Transfer [M11]	28 days	Mon 9/28/26	Wed 11/4/26	Contractor & PRO SME FUND
Project Handover - Closure				
FINAL Update of Central Archive for Project/ Project Closure				
Source Code Handover				
Credentials and Access				
Design Assets and Documentation				
Intellectual Property Handover				


OPTIONAL: Warranty / Support Period - "Requires Contract Amendment between Principles to Contract)				
Contract Management (Project Owner and Contractor)				
Thirty (30) days Free Post Launch [M12]	28 days	Thu 11/5/26	Mon 12/14/26	
Project Technical Team to test Digital Solution and Conduct further UAT				
Prepare and Plan Launch of Website for Client Approval				

Draft Report

5. ROLES AND RESPONSIBILITIES

5.1. The functional working structure proposed for management of the project implementation is documented below;

HIGH LEVEL PLANNING: PROSME PROJECT IMPLEMENTATION AND EXECUTION – “Preliminary Structure for Functional Roles and Responsibilities”

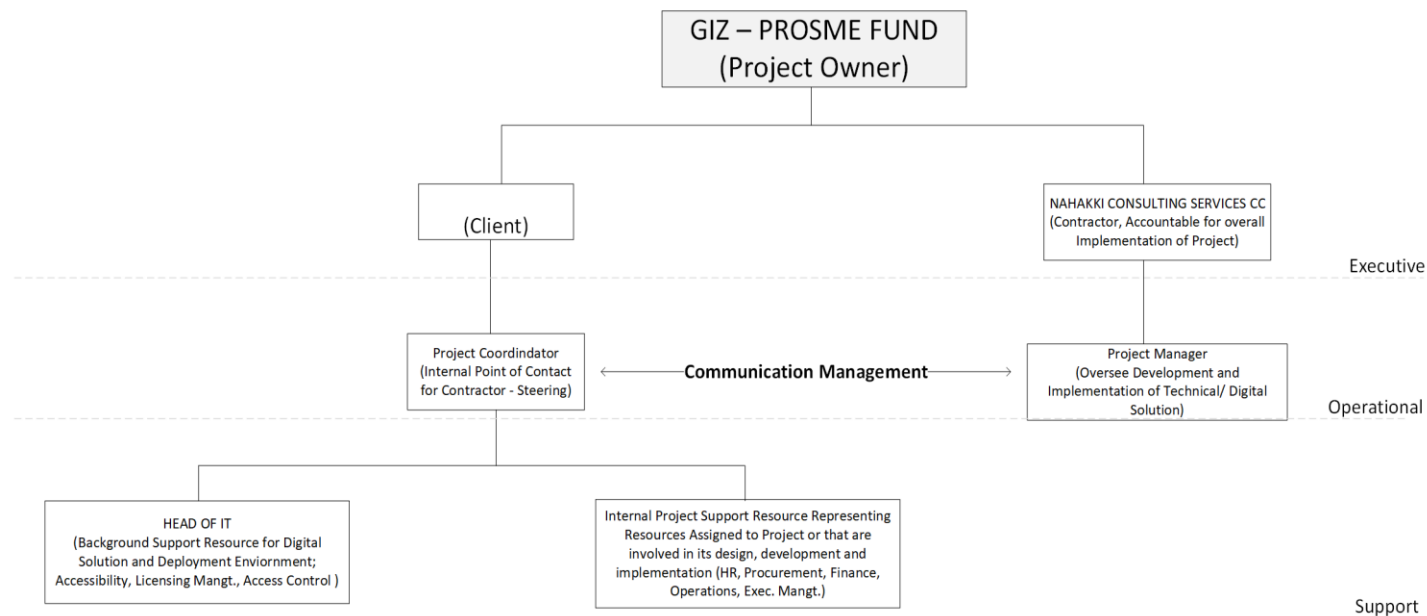

GIZ – PROSME FUND
Project Owner/ TENDER: 7000016311
CLIENT
Primary User -Org (Client), of the Digital Solution being Developed by the Contractor through Tender specified under the Project Owner Function/ Above.
Contractor
NAHAKKI CONSULTING SERVICES CC, responsible - accountable for managing Project and overseeing entire implementation/ Appointed - Contracted by Project Owner
Project Manager/ Project Lead
Responsible person assigned to major project technicalities and overall delivery of digital solution under the Contractor
Project Coordinator
Internal Function to Client, responsible for Communication Management between Client and Contractor. All Communication and Administration of Projects aspects – including updates and reporting shall be conducted through the Project Coordinator appointed by the Client
Project Support Resource
Resource appointed by the Client to support the Project implementation
HEAD of IT (Client)
Responsible for facilitating access to internal IT systems for deploying and hosting solutions, authentication – access control and facilitating hosting

5.2. The Parties are required to review and accept this structure and amend where, necessary. Defining Functional roles is crucial and key element in requirements validation more specifically for managing human resource involvement on the project as its success is effort based.

6. RESOURCES AND BUDGET

6.1. The Project will utilize the required technical, human, software, development and IT infrastructure resources, supported by the Contractor's technical team throughout implementation.

6.2. The financial arrangements are governed by the Agreement signed between the Project Owner and Contractor on 12 August 2026.

6.3. The Parties' signatures confirm acceptance of the agreed terms, conditions and financial obligations, with project resources and expenditure managed accordingly.

Draft Report

7. RISK MANAGEMENT

7.1. Risk Management will form part of the Project's overall Quality Management and weekly project review process. A Risk Register, or equivalent risk management section, shall be incorporated into the Weekly Project Meeting / Status Update Template provided for the Project.

7.2. The purpose is to ensure that risks are not only identified, but are clearly understood, assessed and followed through with appropriate action.

Risk Classification

7.3. Identified risks shall be classified under the following major categories:

Strategic, Scope & Stakeholder Risk	• Project Objectives, Scope, Requirements, Stakeholder Participation, Communication, Approvals, Changes
Design, Functional, & User Experience	• Website design, functionality, usability, content structure, and alignment with user/ client expectations
Technical, Security and Data Risks	• Development, Infrastructure, Integrations, System Compatibility, Data Protection, Security and Access Control
Project Delivery & Resource Risks	• Schedule, Technical Resources, Skills, Capacity, Dependencies and overall implementation coordination
Financial, Commercial and Compliance Risks	• Budget, Contractual matters, additional costs, procurement requirements, and applicable policies and regulations
Quality, Operational and Change Risks	• Testing, Acceptance, defects, implementation, training, user adoption, transition and post - development adoption

Risk Management Structure – Handling Risk

7.4. This section of the document puts emphasis on using risk as a catalyst to improve on the project overall delivery and quality. Structured identification and action is recommended using the structure prescribed; Rather than simply sighting – mentioning/ pointing them out (verbally) and subsequently recording risks. Each material risk should indicate how it may affect project performance and what action is recommended to manage or mitigate it;



Weekly Risk Management

7.4. As part of the weekly project meeting - update and quality management process, identified risks shall be reviewed and updated where necessary using utilities provided – recommended/ prescribed. The weekly updates shall provide sufficient parameters to fully document risks identified and appropriate recommendation to mitigate risk.

7.5. This approach ensures that risk identification is directly connected to project performance, decision-making and corrective action, while maintaining a practical risk management record within the existing weekly project reporting structure.

7.6. Where a risk has a significant potential impact on scope, cost, quality, security, schedule or delivery, it should be escalated to the appropriate Project Owner and Contractor representatives for further consideration and resolution.

7.7. The following additional - supplementary Risk management structure is for reference purposes, to determine the **impact - likelihood** the risk poses to the project including structured guidelines for *fast* decision making;

IMPACT	Significant	Considerable management required	Must manage and monitor risks	Extensive Management essential
	Moderate	Risks may be worth accepting with monitoring	Management effort Worthwhile	Management effort required
	Low	Acceptable Risk	Accept and Monitor Risk	Manage & Monitor Risk
		Low	Moderate	High
	LIKELIHOOD			

Risk Management Principle:

A risk that is identified, assigned and actively monitored can be managed; an unidentified or unmanaged risk can become a project issue, delay or liability.

8. QUALITY MANAGEMENT

8.1. Quality Management shall be applied across the planning, design, development, testing and implementation of the project's major deliverables. The Tender Terms of Reference (ToR) establishes the applicable specifications and expectations for quality, and these shall form the basis for monitoring compliance throughout the project lifecycle.

8.2. The project's Quality Management approach shall include defined standards, compliance checks, reviews, validations, approvals and acceptance procedures. Particular emphasis shall be placed on the continuous assessment of planned deliverables against actual weekly outputs to ensure that deviations are identified early and corrective action is taken.

Quality Monitoring and Reporting

8.3. Weekly quality monitoring shall be supported through standardized tools, including:

- ✓ Weekly project updates and status reports;
- ✓ Deliverable review and verification records;
- ✓ Quality and compliance checklists;
- ✓ Approval and acceptance records; and
- ✓ Supplementary Project Documentation Retention



8.4. All weekly reports should be date-stamped and version controlled to provide a clear audit trail of project progress and decisions.

Central Document Repository

8.5. A central project repository shall be maintained as the authoritative location for project documentation, information and approved deliverables.

8.6. To ensure consistency, document control and accountability, the **Project Coordinator** should be responsible for the administration and maintenance of the central repository. Project Team

members shall submit relevant documents and updates through the agreed communication and document-control process.

- 8.7.[OPTIONAL] An online Excel-based register may be maintained to record documents, deliverables, versions, responsible persons, dates and approval status. Files uploaded to the repository should follow an agreed naming and version-control convention.

Roles, Responsibilities and Communication


- 8.8. For the Quality Management procedures to be effective, all project stakeholders must have a clear understanding of their respective roles, responsibilities, approval authority and reporting obligations, and subsequently be accepted by the Parties – Project Team members.

- 8.9. Reference is made to the Project Structure under section 5 of this document. In order to maintain effective communication; its highly recommended that the Project Team adopt and interactive communication structure between all Team members where necessary, however for formal communication; Communication should take place through the Project Coordinator (Client) and Project Manager (Project Lead - Contractor).

- 8.10. The functional structures noted above shall at their discretion determine communication mediums, availability and any other necessary aspects required in order to achieve effective communication between the Parties.

Central Repository Structure

- 8.11. This structure shall provide a single, controlled source of project information, supporting quality assurance, traceability, accountability and efficient project handover. For the purpose of information integrity, its recommended that all Project Team members have access to this folder with limited privileges (viewing), while the Project Coordinator be assigned upload (write) privileges. The recommended central project repository structure should include, but not be limited to, the following folder structure:

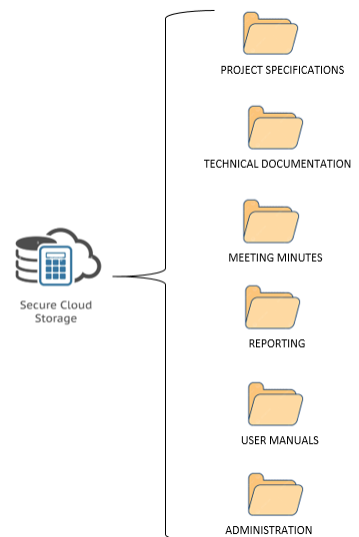

9. COMMUNICATION PLAN

- 9.1. Effective communication is essential to the successful delivery of the Project. Given the 35-day implementation period, communication shall be structured, timely and accessible to the Client, Contractor and relevant stakeholders.
- 9.2. The Project Coordinator and Project Manager should generally be available for project-related communication Monday to Friday, 08:00–17:00, with additional communication taking place where reasonably required to support delivery.

Project Communication Structure

- 9.3. Communication between the Client and Contractor project structures shall include relevant stakeholders as required. The respective teams shall maintain regular engagement to address requirements, queries, decisions, deliverables and emerging issues.
- 9.4. A weekly project meeting, preferably at the end of each working week, shall provide the formal opportunity to review project progress, outstanding matters, risks, deliverables and activities for the following period. The meeting should also provide an opportunity to review and endorse the Weekly Status Report.
- 9.5. Additional meetings or engagements may be arranged where required by the Project Owner, Contractor or Technical Team.

Digital Collaboration

- 9.6. To support a more interactive working environment and improve communication turnaround times, the project team may, at its discretion, make use of appropriate digital collaboration and communication platforms, including readily available or open-source solutions.
- 9.7. Where such a platform is adopted, relevant team members shall be provided with appropriate access and shall use the agreed platform for project-related collaboration, updates, queries and information sharing.
- 9.8. The digital collaboration space should complement, rather than replace, formal project records and approved communication channels.

Email Communication

- 9.9. Official email communication shall be used for formal instructions, approvals, submissions, confirmations, decisions and other matters requiring an auditable record.
- 9.10. Communication shall, where applicable, follow the official contact channels and responsibilities identified elsewhere in this document.

Meetings and Records

- 9.11. Face-to-face meetings are encouraged where they provide practical value. However, Microsoft Teams or other suitable virtual meeting platforms may be used where physical meetings are impractical or where virtual engagement provides a more efficient use of project time.
- 9.12. All formal meetings, whether physical or virtual, shall be appropriately recorded. Meeting records should capture the participants, key matters discussed, decisions, actions, responsible persons and target dates.
- 9.13. Final meeting minutes and action records shall be retained in the designated Meeting Minutes section of the central project repository.

Communication Conduct

- 9.14. All project communication shall be conducted professionally and in accordance with applicable business ethics, Client policies, confidentiality, information security and appropriate use of project resources.
- 9.15. Team members are expected to participate in communication and provide information, decisions or actions within their area of responsibility where required.

Document Naming Convention

- 9.16. To support consistency, traceability and efficient retrieval, project records shall follow a standard naming convention:

<Document / File Name>_<Date>_<Project Team Member Name>

Example:

Weekly Status Report_21-08-2026_Project Coordinator

Where applicable, a version number may be added:

Weekly Status Report_21-08-2026_Project Coordinator_V1.0

- 9.17. The convention should be applied consistently to status reports, meeting minutes, registers, technical documents, submissions and other controlled project records.

10. CHANGE MANAGEMENT

10.1. Change Management shall provide a controlled process for managing changes to the approved project scope, requirements, specifications, deliverables, timelines, processes or implementation arrangements.

10.2. The approved Project Structure and Reference Document shall serve as the project baseline. Any material change shall be identified, assessed, documented and appropriately authorized before being incorporated into the Project.

Change Request

10.3. Where a change is required, the proposed change shall clearly identify:

- ✓ **Area Affected** – The specific requirement, deliverable, activity or project component affected.
- ✓ **Reason for Change** – The motivation or need for the proposed change.
- ✓ **Impact & Risk** – The effect of the change on scope, time, cost, quality, resources, functionality or other dependencies, including the potential consequences of not implementing it.
- ✓ **Proposed Change** – A clear description of what is required.
- ✓ **Resources & Responsibility** – The responsible person/team and any additional resources required.
- ✓ **Integration & Implementation** – How the approved change will be incorporated into the existing project and the proposed implementation timeframe.

10.4. The approved Change Management Form / Template provided through this Document shall be used to record and process change requests.

Assessment and Approval

- 10.5. Each proposed change shall be reviewed to determine its impact on the approved project baseline and whether it can be accommodated within the existing scope and resources.
- 10.6. Changes that materially affect scope, cost, schedule, key deliverables, contractual obligations or project risks shall be referred to the Project Owner and authorized project representatives for consideration and approval.
- 10.7. A change shall not be considered approved solely on the basis of verbal discussion, email communication or meeting discussions. It shall be formally documented and authorized in accordance with the agreed project governance arrangements.

Implementation and Control

- 10.8. Once approved, the change shall be incorporated into the relevant requirements, designs, schedules, specifications, reports and other project records. The Project Coordinator / Project Manager and Contractor shall coordinate implementation in accordance with the approved change.
- 10.9. All Change Management Forms, supporting assessments, approvals and related records shall be retained in the Central Project Repository and managed in accordance with the project's document control and archiving requirements.

Change Management Principle:

Changes should be assessed before implementation, appropriately authorized and fully incorporated into the controlled project baseline to maintain accountability and traceability.

NOTES

[illegible]

Annexures

Draft Report
